



Guidelines for Acquisition Planning

Ceci Albert

John Bergey

Wolf Goethert

Ed Morris

Sponsored by the U.S. Department of Defense
© 2004 by Carnegie Mellon University

Report Documentation Page				Form Approved OMB No. 0704-0188	
Public reporting burden for the collection of information is estimated to average 1 hour per response, including the time for reviewing instructions, searching existing data sources, gathering and maintaining the data needed, and completing and reviewing the collection of information. Send comments regarding this burden estimate or any other aspect of this collection of information, including suggestions for reducing this burden, to Washington Headquarters Services, Directorate for Information Operations and Reports, 1215 Jefferson Davis Highway, Suite 1204, Arlington VA 22202-4302. Respondents should be aware that notwithstanding any other provision of law, no person shall be subject to a penalty for failing to comply with a collection of information if it does not display a currently valid OMB control number.					
1. REPORT DATE JAN 2004		2. REPORT TYPE		3. DATES COVERED 00-00-2004 to 00-00-2004	
4. TITLE AND SUBTITLE Guidelines for Acquisition Planning				5a. CONTRACT NUMBER	
				5b. GRANT NUMBER	
				5c. PROGRAM ELEMENT NUMBER	
6. AUTHOR(S)				5d. PROJECT NUMBER	
				5e. TASK NUMBER	
				5f. WORK UNIT NUMBER	
7. PERFORMING ORGANIZATION NAME(S) AND ADDRESS(ES) Carnegie Mellon University,Software Engineering Institute,Pittsburgh,PA,15213				8. PERFORMING ORGANIZATION REPORT NUMBER	
9. SPONSORING/MONITORING AGENCY NAME(S) AND ADDRESS(ES)				10. SPONSOR/MONITOR'S ACRONYM(S)	
				11. SPONSOR/MONITOR'S REPORT NUMBER(S)	
12. DISTRIBUTION/AVAILABILITY STATEMENT Approved for public release; distribution unlimited					
13. SUPPLEMENTARY NOTES					
14. ABSTRACT					
15. SUBJECT TERMS					
16. SECURITY CLASSIFICATION OF:			17. LIMITATION OF ABSTRACT Same as Report (SAR)	18. NUMBER OF PAGES 19	19a. NAME OF RESPONSIBLE PERSON
a. REPORT unclassified	b. ABSTRACT unclassified	c. THIS PAGE unclassified			

System Acquisition Approach -1

“We Got it Covered” Approach



What software? I am buying a system – my contractor will take care of all of the implementation issues!

System Acquisition Approach -2

“Let’s Cross that Bridge When We Come to It” Approach



Software is inherently flexible – so define the rest of the system first and then we can define and build the software

System Acquisition Approach -3

“Attack the High Risk Issues at the Outset” Approach



Software poses major system risk – give software issues full consideration and adequately address them from the start



Purpose of the Guidelines

Help project managers select and defend acquisition strategies that explicitly consider and mitigate the software risks in their software-intensive system acquisition

- **Provide a framework for effectively reasoning about the software risks in the project**
- **Provide the insights necessary to mitigate those risks in design of the project's acquisition strategy**
- **Create a shared understanding of why specific strategies have been selected from among the myriad of possibilities**



To Mitigate Software Risks

Profile the software risk in the project early - and continuously - so that stakeholders can make reasonable mitigation decisions

Create - and update - the program's acquisition strategy based on an understanding of the program's exposure to software risk

Reason about and defend the efficacy of a given acquisition strategy based on its ability to mitigate the software risk



Determining Exposure to Software Risk


A primary concern in acquisition planning is understanding the degree to which software components in the system pose risk.

The level of software risk depends on

- The amount of software in the system**
- The importance of software performance to system operation**
- The precedence or difficulty of a given software component to build and/or integrate with other system component**




System Software Risk Elements

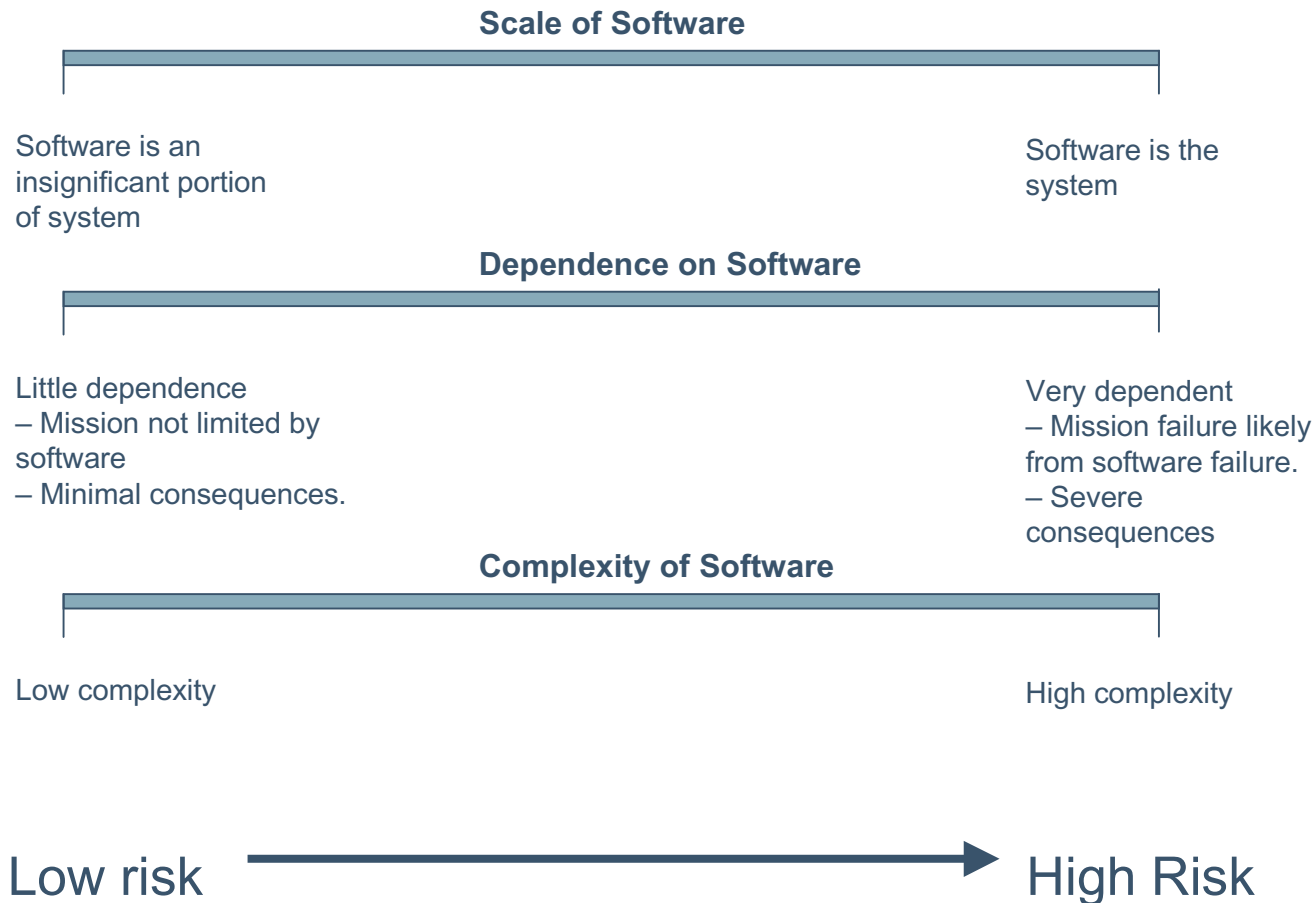




System Software Risk Elements

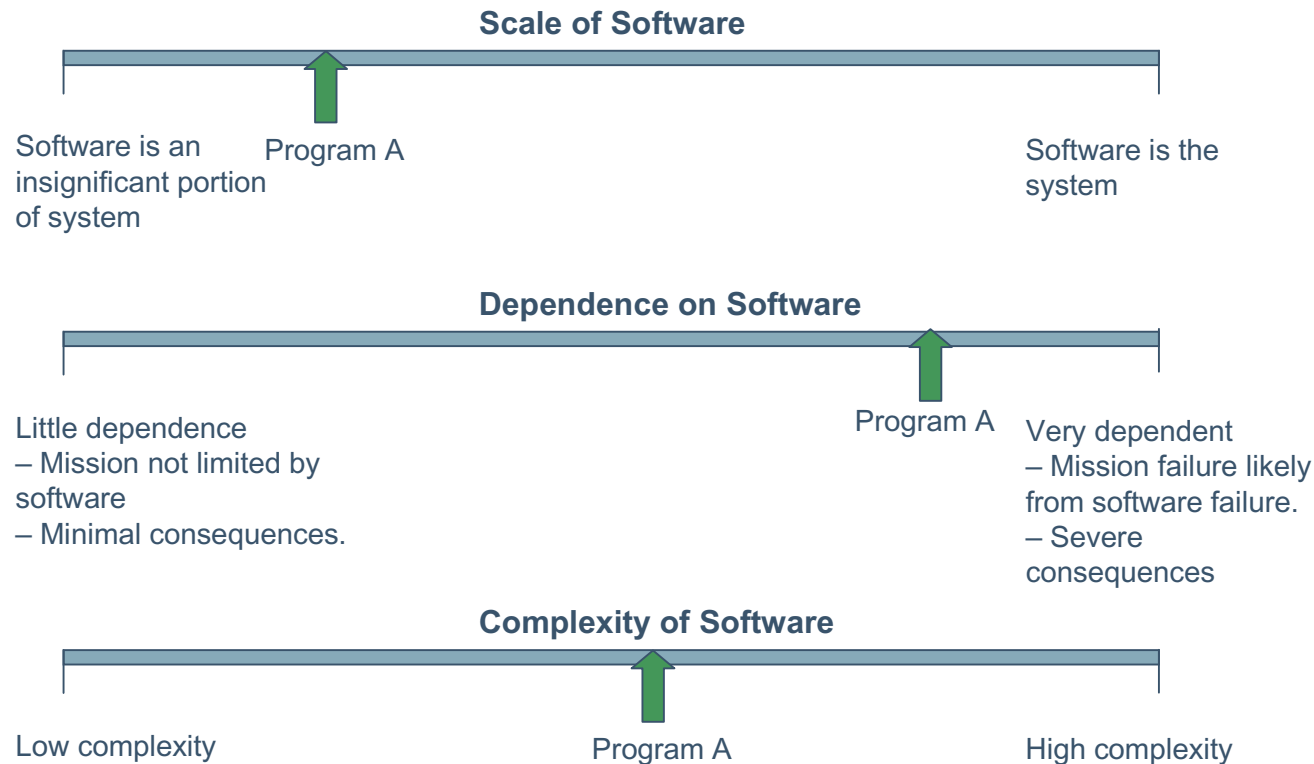


The arrows represent the judgment of the program manager




Elements of Software Risk

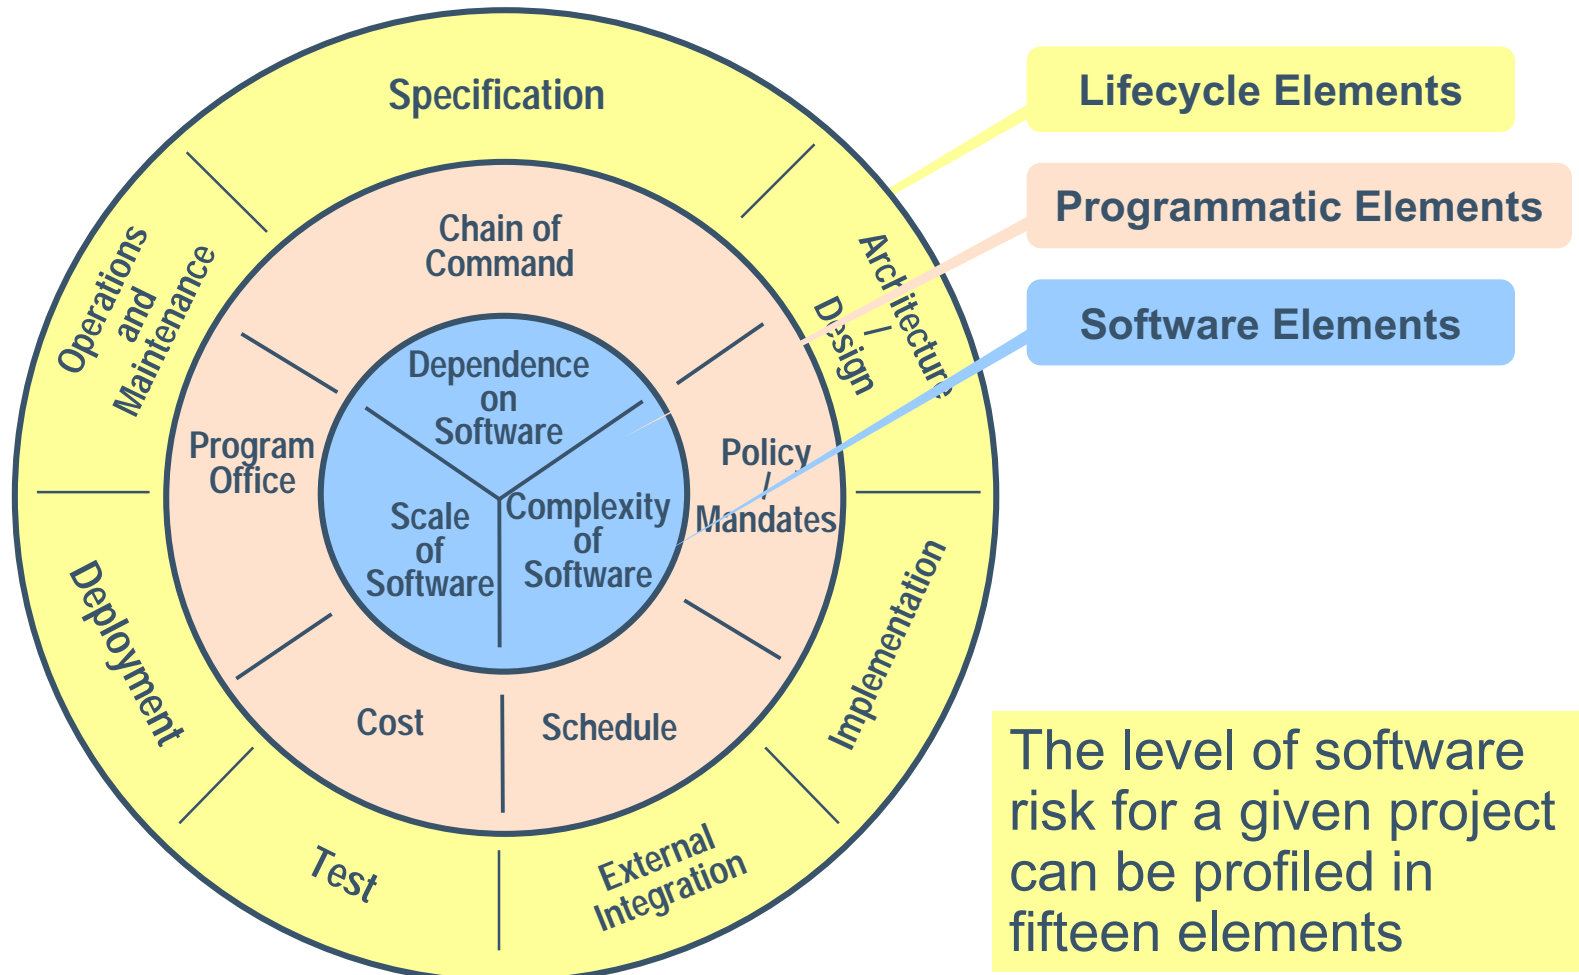

Risk Elements

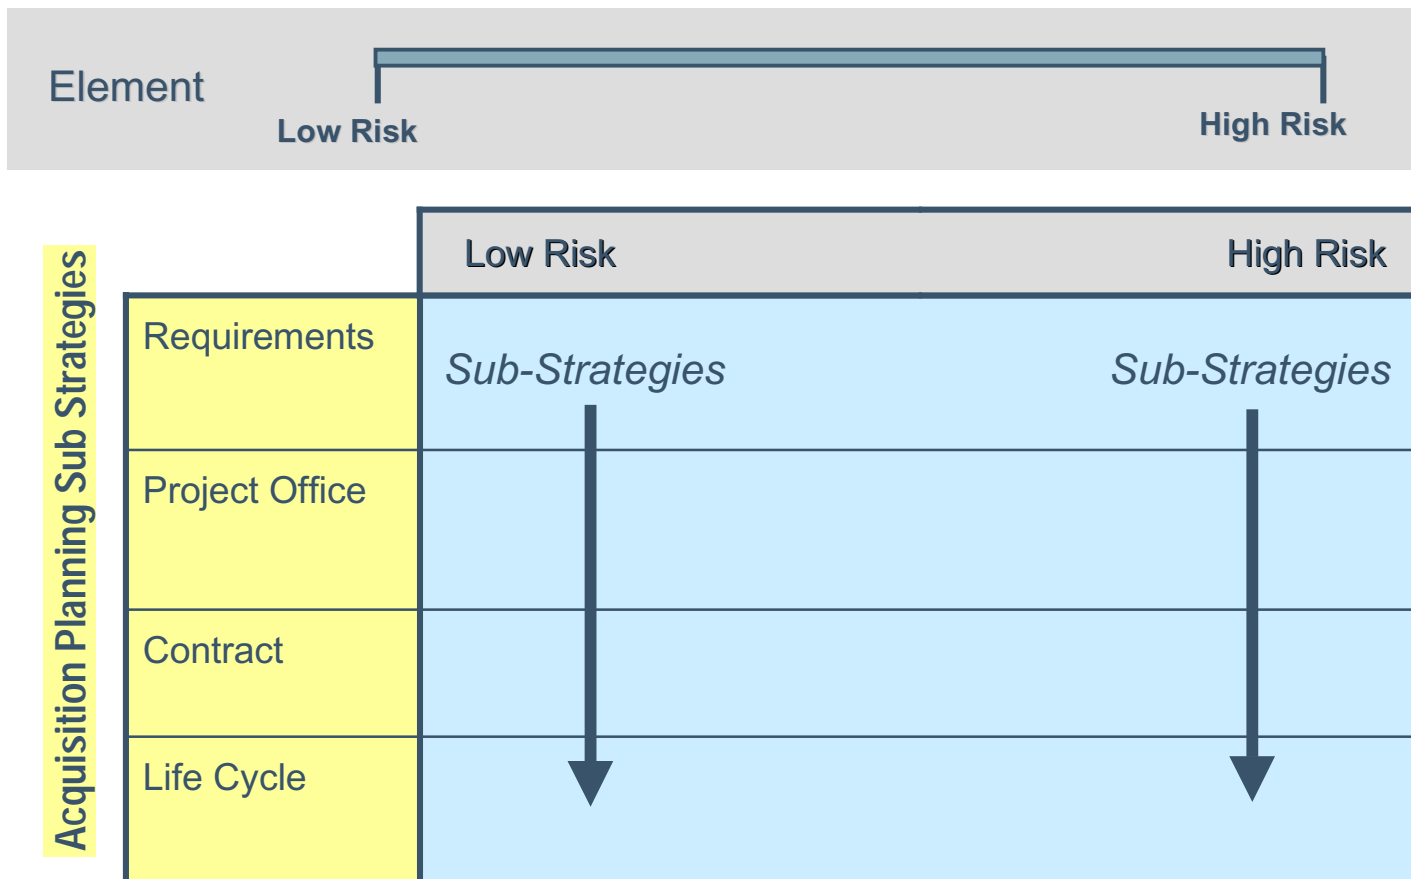

Risk and Acquisition Strategies



Acquisition Planning Sub Strategies	Program A		
	Low Risk		High Risk
	Requirements	<i>Sub-Strategies</i>	<i>Sub-Strategies</i>
	Project Office		
	Contract		
	Life Cycle		

Vertical arrows indicate the flow of sub-strategies from the Requirements row down to the Life Cycle row for each risk level. A green arrow points from the middle Sub-Strategies cell down to the Life Cycle cell, while dark blue arrows point from the Low Risk and High Risk Sub-Strategies cells down to the Life Cycle cell.



For Example: Specification Risks

Stable, fully defined, unambiguous, consistent, complete, testable software requirements are rare.

- **Some requirements are firm from the start**
- **Some requirements cannot be defined until other things about the system are known**
- **Some requirements may be in a constant state of flux as technology, off-the-shelf product, mission needs (or the understanding of what is needed) evolve.**

Trying to fully define software requirements too early or trying to limit requirements changes in a changing environment may be riskier than having flexible requirements.

The acquisition strategy needs to accommodate the degree to which requirements can or should change.



Well-defined, complete,
and stable

Incomplete or volatile

Specification

	Well defined and stable	Incomplete or volatile
Reqmts	§ Implement strong process oversight to control changes	§ Flexible, prioritized and negotiated requirements § Nimble process to manage and communicate changes
Project Office	§ Limited oversight required	§ Increased need for engineering staff to monitor system design/progress
Contract	§ Consider fixed price contract	§ Avoid completion contracts (use Cost-plus services contract?) § Offer incentives for delivered system performance
Life Cycle	§ "Waterfall" approach § Favorable terms for O&M may be defined with development contract	§ Spiral approach § May not be able to award an O&M contract better understood



<div>Well-defined, complete, and stable</div> <div>Selected requirements depend on volatile technology</div> <div>Incomplete or volatile</div>		
<h1>Specification</h1>		
	Well defined and stable	Incomplete or volatile
Reqmts	§ Implement strong process oversight to control changes	§ Flexible, prioritized and negotiated requirements § Nimble process to manage and communicate changes
Project Office	§ Limited oversight required	§ Increased need for engineering staff to monitor system design/progress
Contract	§ Consider fixed price contract	§ Avoid completion contracts (use Cost-plus services contract?) § Offer incentives for delivered system performance
Life Cycle	§ “Waterfall” approach § Favorable terms for O&M may be defined with development contract	§ Spiral approach § May not be able to award an O&M contract better understood




Specification

	Well defined and stable	Strategy A2	Incomplete or volatile
Reqmts	§ Implement strong process oversight to control changes	• Isolate the affected requirements so the changes are obvious	§ Flexible, prioritized and negotiated requirements § Nimble process to manage and communicate changes
Project Office	§ Limited oversight required	• Track technology evolution to identify commitment point	§ Increased need for engineering staff to monitor system design/progress
Contract	§ Consider fixed price contract	• Separately price unknown requirements – incentivize low cost	§ Avoid completion contracts (use Cost-plus services contract?) § Offer incentives for delivered system performance
Life Cycle	§ “Waterfall” approach § Favorable terms for O&M may be defined with development contract	• Plan and budget for changes across the life of the system	§ Spiral approach § May not be able to award an O&M contract better understood



Project Profile (Composite of Elements)

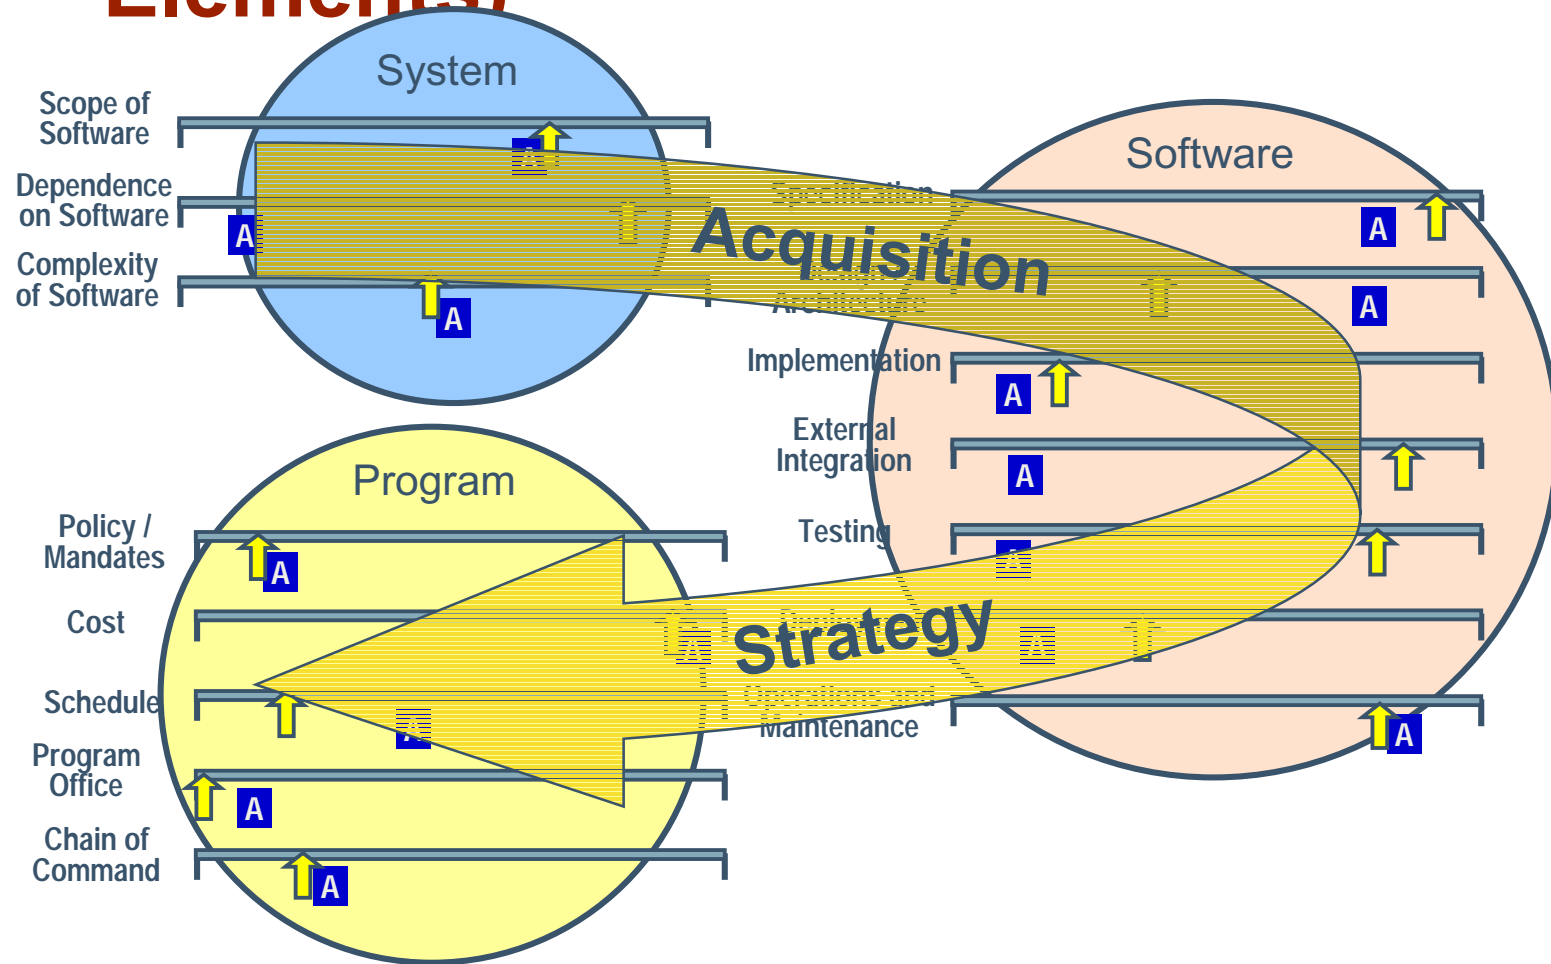



Next Steps in Use of Sliders

Validate the approach and the set of sliders by profiling the software risk in selected Army programs using the sliders

Show how each program's current acquisition strategy relates to their identified software risk

Pilot use of Guidelines in a new start

Document the Guidelines



Carnegie Mellon
Software Engineering Institute

Contact Information

Ceci Albert
cca@sei.cmu.edu
